


NexusNotes

Ramasani Adi Pranav – 24CSB0A57


Syed Mohammad Sami – 24CSB0A77

Janapala Harshavardhan Reddy – 24CSB0A28


1. Create Summary Task




2. Create key tasks




3. Create key tasks dependencies





4. Insert sub-tasks and indent

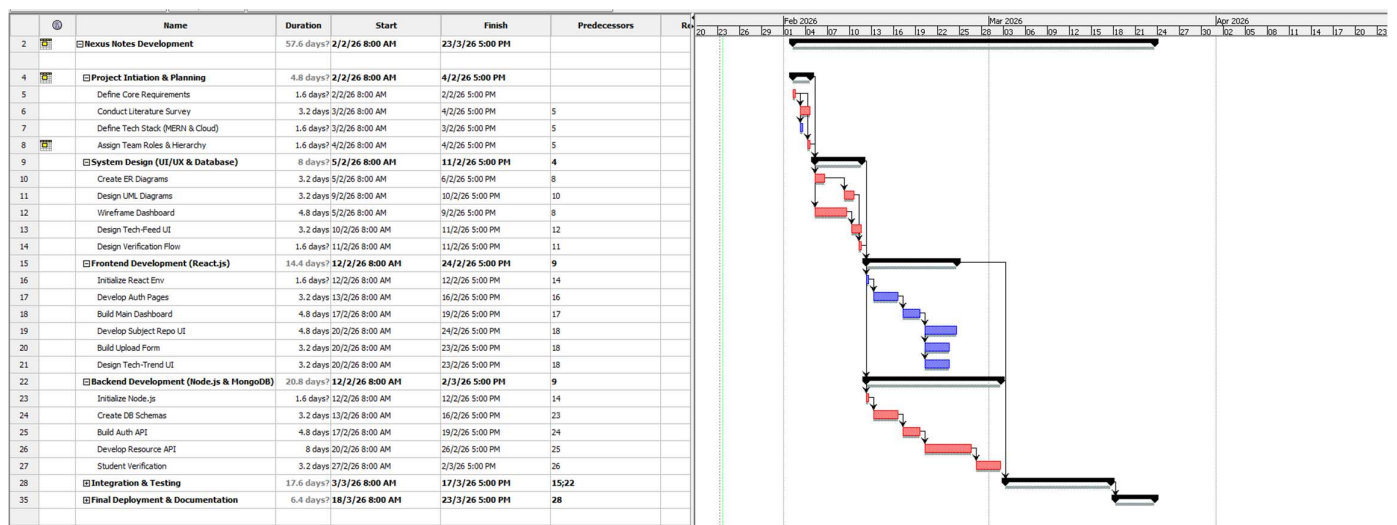

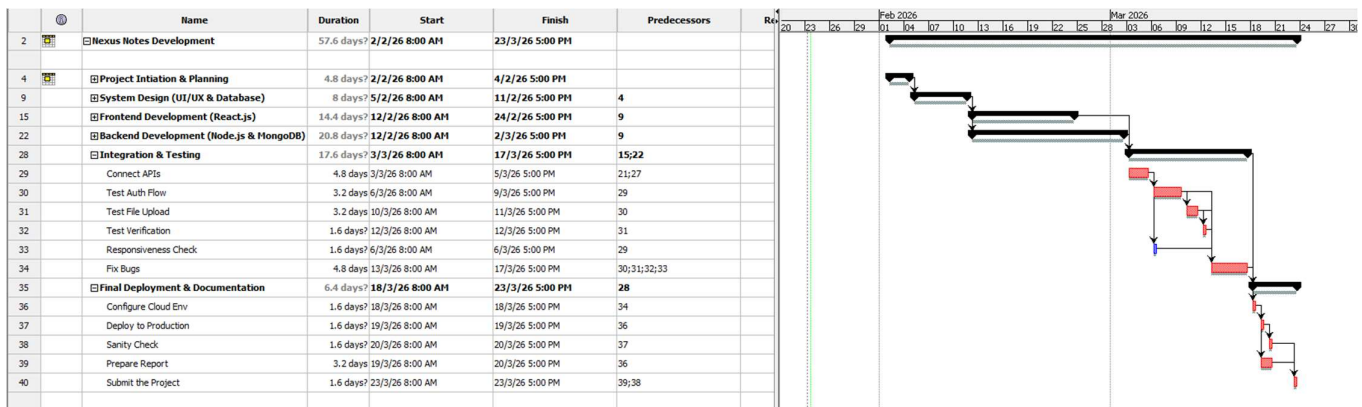

5. Create sub-tasks dependencies

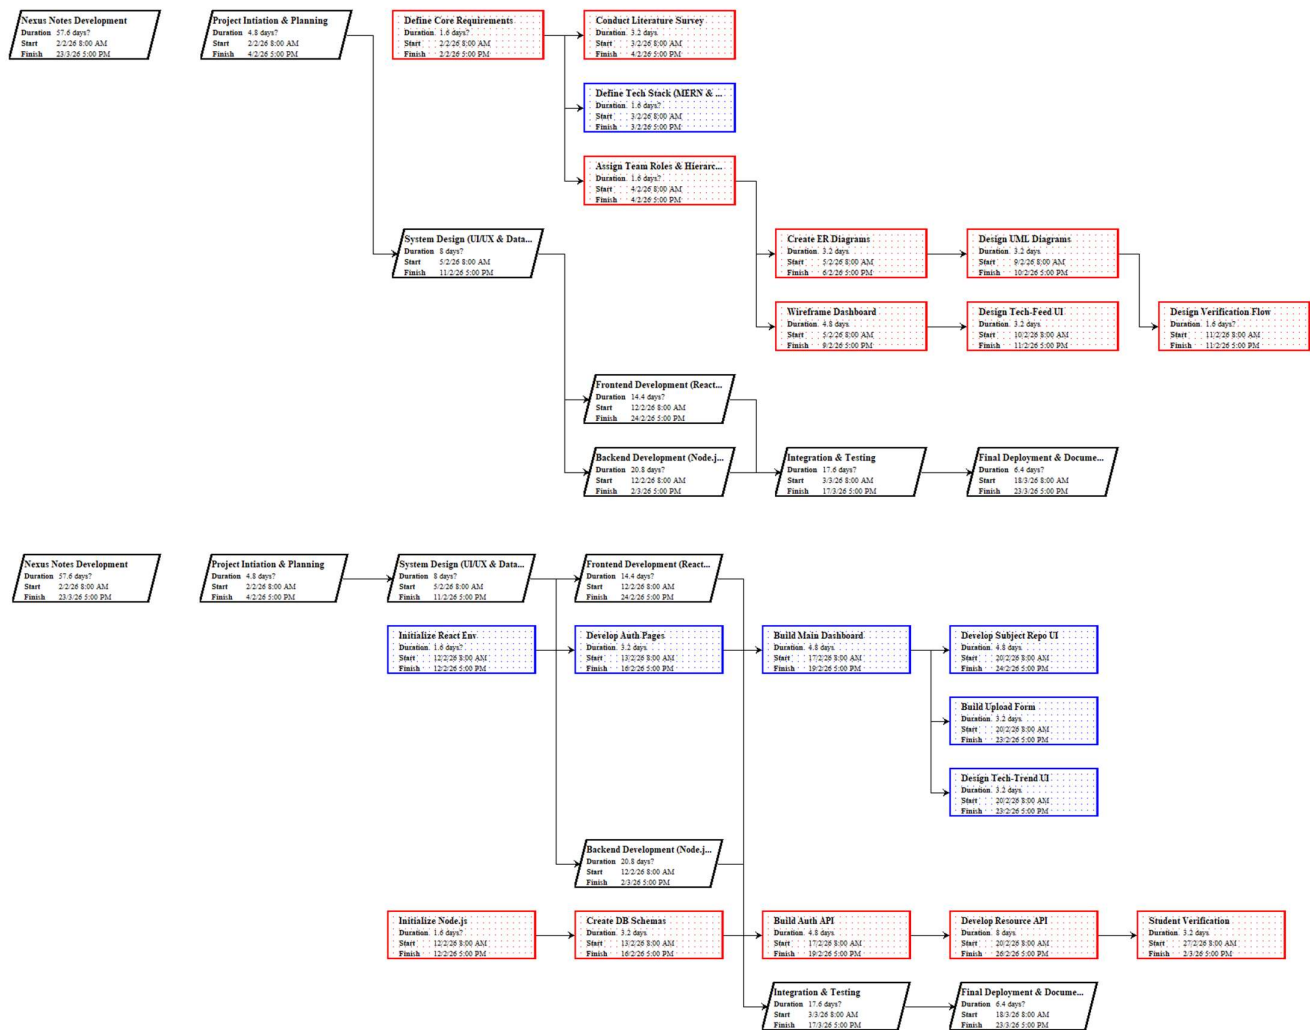

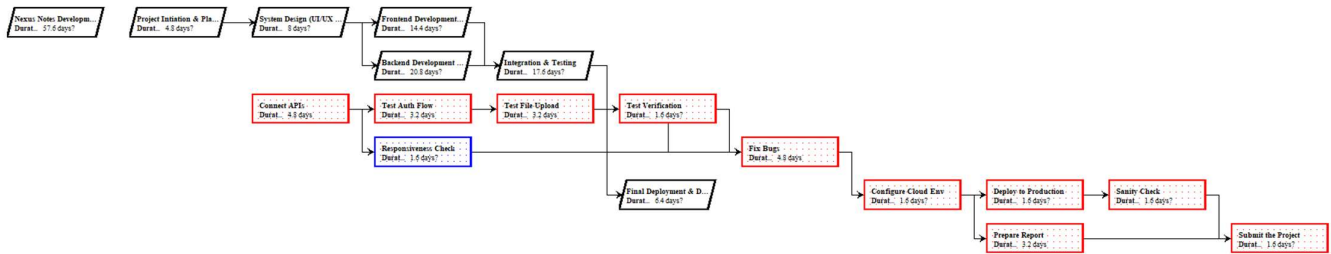

6. Estimate duration to all the created tasks

		Name	Duration	Start	Finish	Pr
2		Nexus Notes Development	57.6 days?	2/2/26 8:00 AM	23/3/26 5:00 PM	
4		Project Initiation & Planning	4.8 days?	2/2/26 8:00 AM	4/2/26 5:00 PM	
9		System Design (UI/UX & Database)	8 days?	5/2/26 8:00 AM	11/2/26 5:00 PM	4
15		Frontend Development (React.js)	14.4 days?	12/2/26 8:00 AM	24/2/26 5:00 PM	9
22		Backend Development (Node.js & MongoDB)	20.8 days?	12/2/26 8:00 AM	2/3/26 5:00 PM	9
28		Integration & Testing	17.6 days?	3/3/26 8:00 AM	17/3/26 5:00 PM	15;22
35		Final Deployment & Documentation	6.4 days?	18/3/26 8:00 AM	23/3/26 5:00 PM	28

7. Change Working Calendar

Change Working Calendar

For: Work

☐ Use default
☐ Non-working time
☐ Non-default working

From: To:

January 2026
 S M T W T F S
 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31

February 2026
 S M T W T F S
 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28

April 2026
 M T W T F S
 1 2 3 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30

Duration Settings
 These settings only apply to durations
 Hours per day : 5
 Hours per week : 40
 Days per month : 20

OK Cancel Help

New... Options... OK Cancel Help

8. Save baseline

Save Baseline

Baseline: Baseline

For:

☒ Entire Project

☐ Selected Tasks

OK Cancel Help

9. Insert new columns (Deadlines, Total Slack, Cost, Work., etc.)

		Name	Duration	Start	Finish	Predecesso...	Resource Names	Work	Deadline	Constraint Date	Total Slack
2		Nexus Notes Developme	52.533 days...	2/2/26 8:00 AM	18/3/26 3:40 PM			472 hours		1/2/26 8:00 AM	0 days
4		Project Initiation & Pla	4.8 days?	2/2/26 8:00 AM	4/2/26 5:00 PM			40 hours		1/2/26 8:00 AM	0 days
5		Define Core Requirement	1.067 days?	2/2/26 8:00 AM	2/2/26 2:20 PM		Adi[50%];Sami[50%];Harsha[...	8 hours	3/2/26 5:00 PM		0.533 days
6		Conduct Literature Surve	3.2 days	2/2/26 2:20 PM	4/2/26 2:20 PM	5	Adi;Sami[50%]	16 hours	4/2/26 5:00 PM		0.533 days
7		Define Tech Stack (MERN	1.6 days?	2/2/26 2:20 PM	3/2/26 2:20 PM	5	Harsha	8 hours	4/2/26 5:00 PM		2.133 days
8		Assign Team Roles & Hier	1.6 days?	4/2/26 8:00 AM	4/2/26 5:00 PM	5	Adi	8 hours	4/2/26 5:00 PM	4/2/26 8:00 AM	0 days
9		System Design (UI/UX)	8 days?	5/2/26 8:00 AM	11/2/26 5:00 PM	4		80 hours			0 days
10		Create ER Diagrams	3.2 days	5/2/26 8:00 AM	6/2/26 5:00 PM	8	Sami	16 hours	6/2/26 5:00 PM		0 days
11		Design UML Diagrams	3.2 days	9/2/26 8:00 AM	10/2/26 5:00 PM	10	Adi	16 hours	11/2/26 5:00 PM		0 days
12		Wireframe Dashboard	4.8 days	5/2/26 8:00 AM	9/2/26 5:00 PM	8	Harsha	24 hours	9/2/26 5:00 PM		0 days
13		Design Tech-Feed UI	3.2 days	10/2/26 8:00 AM	11/2/26 5:00 PM	12	Harsha	16 hours	12/2/26 5:00 PM		0 days
14		Design Verification Flow	1.6 days?	11/2/26 8:00 AM	11/2/26 5:00 PM	11	Sami	8 hours	12/2/26 5:00 PM		0 days
15		Frontend Development	14.4 days?	12/2/26 8:00 AM	24/2/26 5:00 PM	9		104 hours	27/2/26 5:00 PM		6.4 days
16		Initialize React Env	1.6 days?	12/2/26 8:00 AM	12/2/26 5:00 PM	14	Harsha	8 hours	13/2/26 5:00 PM		6.4 days
17		Develop Auth Pages	3.2 days	13/2/26 8:00 AM	16/2/26 5:00 PM	16	Sami	16 hours			6.4 days
18		Build Main Dashboard	4.8 days	17/2/26 8:00 AM	19/2/26 5:00 PM	17	Harsha	24 hours	20/2/26 5:00 PM		6.4 days
19		Develop Subject Repo UI	4.8 days	20/2/26 8:00 AM	24/2/26 5:00 PM	18	Adi	24 hours			6.4 days
20		Build Upload Form	3.2 days	20/2/26 8:00 AM	23/2/26 5:00 PM	18	Adi	16 hours	25/2/26 5:00 PM		8 days
21		Design Tech-Trend UI	3.2 days	20/2/26 8:00 AM	23/2/26 5:00 PM	18	Sami	16 hours	27/2/26 5:00 PM		8 days
22		Backend Development	20.8 days?	12/2/26 8:00 AM	2/3/26 5:00 PM	9		104 hours	3/3/26 5:00 PM		0 days
23		Initialize Node.js	1.6 days?	12/2/26 8:00 AM	12/2/26 5:00 PM	14	Sami	8 hours	28/2/26 5:00 PM		0 days
24		Create DB Schemas	3.2 days	13/2/26 8:00 AM	16/2/26 5:00 PM	23	Adi	16 hours	28/2/26 5:00 PM		0 days
25		Build Auth API	4.8 days	17/2/26 8:00 AM	19/2/26 5:00 PM	24	Sami	24 hours			0 days
26		Develop Resource API	8 days	20/2/26 8:00 AM	26/2/26 5:00 PM	25	Adi	40 hours	28/2/26 5:00 PM		0 days
27		Student Verification	3.2 days	27/2/26 8:00 AM	2/3/26 5:00 PM	26	Sami	16 hours			0 days
28		Integration & Testing	14.4 days?	3/3/26 8:00 AM	13/3/26 5:00 PM	15;22		96 hours			0 days
29		Connect APIs	4.8 days	3/3/26 8:00 AM	5/3/26 5:00 PM	21;27	Sami	24 hours			0 days
30		Test Auth Flow	3.2 days	6/3/26 8:00 AM	9/3/26 5:00 PM	29	Harsha	16 hours	15/3/26 5:00 PM		0 days
31		Test File Upload	3.2 days	10/3/26 8:00 AM	11/3/26 5:00 PM	30	Adi	16 hours			0 days
32		Test Verification	1.6 days?	12/3/26 8:00 AM	12/3/26 5:00 PM	31	Adi	8 hours			0 days
33		Responsiveness Check	1.6 days?	6/3/26 8:00 AM	6/3/26 5:00 PM	29	Harsha	8 hours			6.4 days
34		Fix Bugs	1.6 days	13/3/26 8:00 AM	13/3/26 5:00 PM	30;31;32;33	Adi;Harsha;Sami	24 hours			0 days

11. Update the Constraint Type of some tasks and verify the same on the Gantt chart

	⊞	Name	Duration	Start	Finish	Predecessor	Resource Names	Work	Deadline	Constraint Date
2	📅	Backend Notes Development	52.533 days	2/2/26 8:00 AM	18/3/26 3:40 PM			472 hours		1/2/26 8:00 AM
4	📅	Project Initiation & Planning	4.8 days	2/2/26 8:00 AM	4/2/26 5:00 PM			40 hours		1/2/26 8:00 AM
5		Define Core Requirements	1.067 days	2/2/26 8:00 AM	2/2/26 2:20 PM		Adi[50%];Sami[50%];Harsha[50%]	8 hours	3/2/26 5:00 PM	
6		Conduct Literature Survey	3.2 days	2/2/26 2:20 PM	4/2/26 2:20 PM	5	Adi;Sami[50%]	16 hours	4/2/26 5:00 PM	
7		Define Tech Stack (MERN)	1.6 days	2/2/26 2:20 PM	3/2/26 2:20 PM	5	Harsha	8 hours	4/2/26 5:00 PM	
8	📅	Assign Team Roles & Hierarchy	1.6 days	4/2/26 8:00 AM	4/2/26 5:00 PM	5	Adi	8 hours	4/2/26 5:00 PM	4/2/26 8:00 AM
9	📅	System Design (UI/UX)	8 days	5/2/26 8:00 AM	11/2/26 5:00 PM	4		80 hours		
10		Create ER Diagrams	3.2 days	5/2/26 8:00 AM	6/2/26 5:00 PM	8	Sami	16 hours	6/2/26 5:00 PM	
11		Design UML Diagrams	3.2 days	9/2/26 8:00 AM	10/2/26 5:00 PM	10	Adi	16 hours	11/2/26 5:00 PM	
12		Wireframe Dashboard	4.8 days	5/2/26 8:00 AM	9/2/26 5:00 PM	8	Harsha	24 hours	9/2/26 5:00 PM	
13		Design Tech-Feed UI	3.2 days	10/2/26 8:00 AM	11/2/26 5:00 PM	12	Harsha	16 hours	12/2/26 5:00 PM	


12. Update the percent complete of some tasks and verify the same on the Gantt chart

22	📅	Backend Development	20.8 days	12/2/26 8:00 AM	2/3/26 5:00 PM	9		104 hours	3/3/26 5:00 PM	0 days
23		Initialize Node.js	1.6 days	12/2/26 8:00 AM	12/2/26 5:00 PM	14	Sami	8 hours	28/2/26 5:00 PM	0 days
24		Create DB Schemas	3.2 days	13/2/26 8:00 AM	16/2/26 5:00 PM	23	Adi	16 hours	28/2/26 5:00 PM	0 days
25		Build Auth API	4.8 days	17/2/26 8:00 AM	19/2/26 5:00 PM	24	Sami	24 hours		0 days
26		Develop Resource API	8 days	20/2/26 8:00 AM	26/2/26 5:00 PM	25	Adi	40 hours	28/2/26 5:00 PM	0 days
27		Student Verification	3.2 days	27/2/26 8:00 AM	2/3/26 5:00 PM	26	Sami	16 hours		0 days
28	📅	Integration & Testing	14.4 days	3/3/26 8:00 AM	13/3/26 5:00 PM	15;22		96 hours		0 days
29		Connect APIs	4.8 days	3/3/26 8:00 AM	5/3/26 5:00 PM	21;27	Sami	24 hours		0 days
30		Test Auth Flow	3.2 days	6/3/26 8:00 AM	9/3/26 5:00 PM	29	Harsha	16 hours	15/3/26 5:00 PM	0 days
31		Test File Upload	3.2 days	10/3/26 8:00 AM	11/3/26 5:00 PM	30	Adi	16 hours		0 days
32		Test Verification	1.6 days	12/3/26 8:00 AM	12/3/26 5:00 PM	31	Adi	8 hours		0 days
33		Responsiveness Check	1.6 days	6/3/26 8:00 AM	6/3/26 5:00 PM	29	Harsha	8 hours		6.4 days
34		Fix Bugs	1.6 days	13/3/26 8:00 AM	13/3/26 5:00 PM	30;31;32;33	Adi;Harsha;Sami	24 hours		0 days
35	📅	Final Deployment & Documentation	4.533 days	16/3/26 8:00 AM	18/3/26 3:40 PM	28		48 hours		0 days
36		Configure Cloud Env	0.8 days	16/3/26 8:00 AM	16/3/26 1:00 PM	34	Adi;Sami	8 hours		0 days
37		Deploy to Production	0.533 days	16/3/26 1:00 PM	16/3/26 3:40 PM	36	Adi;Harsha;Sami	8 hours		1.067 days
38		Sanity Check	1.6 days	16/3/26 3:40 PM	17/3/26 3:40 PM	37	Harsha	8 hours		1.067 days
39		Prepare Report	3.2 days	16/3/26 1:00 PM	18/3/26 1:00 PM	36	Adi	16 hours		0 days
40		Submit the Project	0.533 days	18/3/26 1:00 PM	18/3/26 3:40 PM	39;38	Adi;Harsha;Sami	8 hours		0 days

13. Create Resources and set the Group and Rate

⊞	Name	RBS	Type	E-mail Address	Material Label	Initials	Group	Max. Units	Standard Rate	Overtime Rate	Cost Per Use	Accrue At
1	Adi		Work			A	Full Stack	100%	Rs.0.00/hour	Rs.0.00/hour	Rs.0.00/Prorated	5
2	Sami		Work			S	Core Dev	100%	Rs.0.00/hour	Rs.0.00/hour	Rs.0.00/Prorated	5
3	Harsha		Work			H	UI/UX	100%	Rs.0.00/hour	Rs.0.00/hour	Rs.0.00/Prorated	5
4	Hosting Server		Material		Cloud	H			Rs.0.00		Rs.0.00/Prorated	

14. Create a resource hierarchy (like who should report to whom)

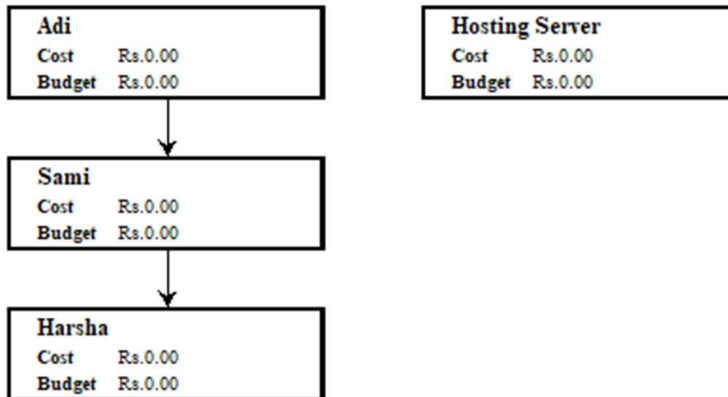

15. Create Materials and set a cost per use


	⊕	Name	RBS	Type	E-mail Address	Material Label	Initials	Group	Max. Units	Standard Rate	Overtime Rate	Cost Per Use	Accrue At
1	⊕	Adi		Work			A	Full Stack	100%	Rs.0.00/hour	Rs.0.00/hour	Rs.0.00 Prorated	\$
2	⊕	Sami		Work			S	Core Dev	100%	Rs.0.00/hour	Rs.0.00/hour	Rs.0.00 Prorated	\$
3	⊕	Harsha		Work			H	UI/UX	100%	Rs.0.00/hour	Rs.0.00/hour	Rs.0.00 Prorated	\$
4		Hosting Server		Material		Cloud	H			Rs.0.00		Rs.0.00 Prorated	

16. Assign Resources to the tasks and verify the same on the Gantt chart


	⊕	Name	Duration	Start	Finish	Predecesso...	Resource Names
2	📅	⊖ Nexus Notes Development	52.533 days	2/2/26 8:00 AM	18/3/26 3:40 PM		
4	📅	⊖ Project Initiation & Planning	4.8 days	2/2/26 8:00 AM	4/2/26 5:00 PM		
5		Define Core Requirement	1.067 days	2/2/26 8:00 AM	2/2/26 2:20 PM		Adi[50%];Sami[50%];Harsha[50%]
6		Conduct Literature Survey	3.2 days	2/2/26 2:20 PM	4/2/26 2:20 PM	5	Adi;Sami[50%]
7		Define Tech Stack (MERN)	1.6 days	3/2/26 2:20 PM	3/2/26 2:20 PM	5	Harsha
8	📅	Assign Team Roles & Responsibilities	1.6 days	4/2/26 8:00 AM	4/2/26 5:00 PM	5	Adi
9	📅	⊖ System Design (UI/UX)	8 days	5/2/26 8:00 AM	11/2/26 5:00 PM	4	
10		Create ER Diagrams	3.2 days	5/2/26 8:00 AM	6/2/26 5:00 PM	8	Sami
11		Design UML Diagrams	3.2 days	9/2/26 8:00 AM	10/2/26 5:00 PM	10	Adi
12		Wireframe Dashboard	4.8 days	5/2/26 8:00 AM	9/2/26 5:00 PM	8	Harsha
13		Design Tech-Freel UI	3.2 days	10/2/26 8:00 AM	11/2/26 5:00 PM	12	Harsha
14		Design Verification Flow	1.6 days	11/2/26 8:00 AM	11/2/26 5:00 PM	11	Sami
15	📅	⊖ Frontend Development	14.4 days	12/2/26 8:00 AM	24/2/26 5:00 PM	9	
16		Initialize React Env	1.6 days	12/2/26 8:00 AM	12/2/26 5:00 PM	14	Harsha
17		Develop Auth Pages	3.2 days	13/2/26 8:00 AM	16/2/26 5:00 PM	16	Sami
18		Build Main Dashboard	4.8 days	17/2/26 8:00 AM	19/2/26 5:00 PM	17	Harsha
19		Develop Subject Repo UI	4.8 days	20/2/26 8:00 AM	24/2/26 5:00 PM	18	Adi
20		Build Upload Form	3.2 days	20/2/26 8:00 AM	23/2/26 5:00 PM	18	Adi
21		Design Tech-Trend UI	3.2 days	20/2/26 8:00 AM	23/2/26 5:00 PM	18	Sami
22	📅	⊖ Backend Development	20.8 days	12/2/26 8:00 AM	2/3/26 5:00 PM	9	
23		Initialize Node.js	1.6 days	12/2/26 8:00 AM	12/2/26 5:00 PM	14	Sami
24		Create DB Schemas	3.2 days	13/2/26 8:00 AM	16/2/26 5:00 PM	23	Adi
25		Build Auth API	4.8 days	17/2/26 8:00 AM	19/2/26 5:00 PM	24	Sami
26		Develop Resource API	8 days	20/2/26 8:00 AM	26/2/26 5:00 PM	25	Adi
27		Student Verification	3.2 days	27/2/26 8:00 AM	2/3/26 5:00 PM	26	Sami
28	📅	⊖ Integration & Testing	14.4 days	3/3/26 8:00 AM	13/3/26 5:00 PM	15;22	
29		Connect APIs	4.8 days	3/3/26 8:00 AM	5/3/26 5:00 PM	21;27	Sami
30		Test Auth Flow	3.2 days	6/3/26 8:00 AM	9/3/26 5:00 PM	29	Harsha
31		Test File Upload	3.2 days	10/3/26 8:00 AM	11/3/26 5:00 PM	30	Adi
32		Test Verification	1.6 days	12/3/26 8:00 AM	12/3/26 5:00 PM	31	Adi
33		Responsiveness Check	1.6 days	8/3/26 8:00 AM	6/3/26 5:00 PM	29	Harsha
34		Fix Bugs	1.6 days	13/3/26 8:00 AM	13/3/26 5:00 PM	30;31;32;33	Adi;Harsha;Sami

22	Backend Development	20.8 days?	12/2/26 8:00 AM	2/3/26 5:00 PM	9	
23	Initialize Node.js	1.6 days?	12/2/26 8:00 AM	12/2/26 5:00 PM	14	Sami
24	Create DB Schemas	3.2 days	13/2/26 8:00 AM	16/2/26 5:00 PM	23	Adi
25	Build Auth API	4.8 days	17/2/26 8:00 AM	19/2/26 5:00 PM	24	Sami
26	Develop Resource API	8 days	20/2/26 8:00 AM	26/2/26 5:00 PM	25	Adi
27	Student Verification	3.2 days	27/2/26 8:00 AM	2/3/26 5:00 PM	26	Sami
28	Integration & Testing	14.4 days?	3/3/26 8:00 AM	13/3/26 5:00 PM	15;22	
29	Connect APIs	4.8 days	3/3/26 8:00 AM	5/3/26 5:00 PM	21;27	Sami
30	Test Auth Flow	3.2 days	6/3/26 8:00 AM	9/3/26 5:00 PM	29	Harsha
31	Test File Upload	3.2 days	10/3/26 8:00 AM	11/3/26 5:00 PM	30	Adi
32	Test Verification	1.6 days?	12/3/26 8:00 AM	12/3/26 5:00 PM	31	Adi
33	Responsiveness Check	1.6 days?	6/3/26 8:00 AM	6/3/26 5:00 PM	29	Harsha
34	Fix Bugs	1.6 days	13/3/26 8:00 AM	13/3/26 5:00 PM	30;31;32;33	Adi;Harsha;Sami
35	Final Deployment & Do	4.533 days?	16/3/26 8:00 AM	18/3/26 3:40 PM	28	
36	Configure Cloud Env	0.8 days?	16/3/26 8:00 AM	16/3/26 1:00 PM	34	Adi;Sami
37	Deploy to Production	0.533 days?	16/3/26 1:00 PM	16/3/26 3:40 PM	36	Adi;Harsha;Sami
38	Sanity Check	1.6 days?	16/3/26 3:40 PM	17/3/26 3:40 PM	37	Harsha
39	Prepare Report	3.2 days	16/3/26 1:00 PM	18/3/26 1:00 PM	36	Adi
40	Submit the Project	0.533 days?	18/3/26 1:00 PM	18/3/26 3:40 PM	39;38	Adi;Harsha;Sami

17. View histogram and check if there is any work overhead

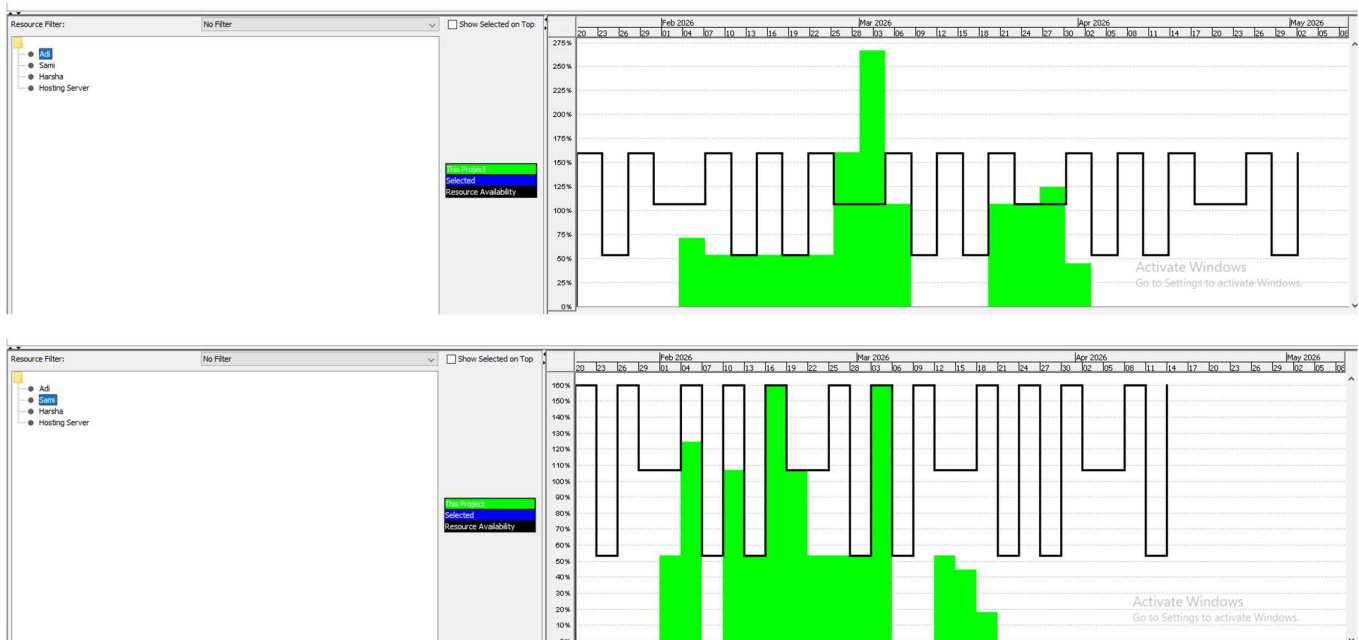

18.If any work overhead then resolve it

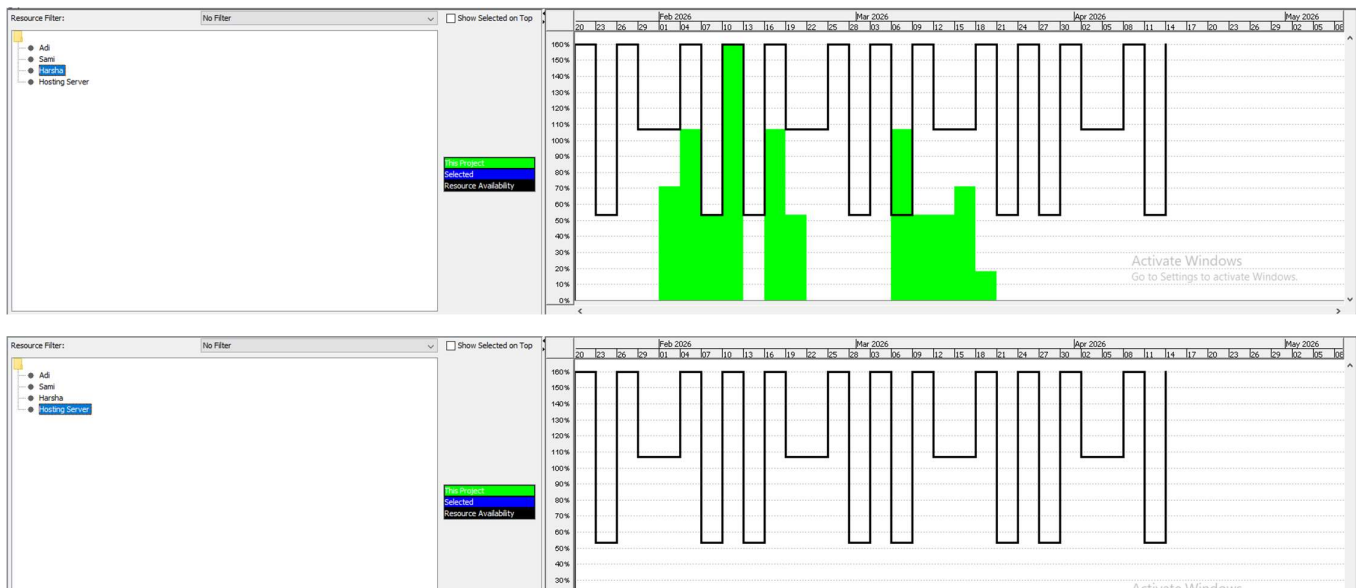

19.Explore other options in the View tab (WBS,RBS, Network Diagram, etc.)

